



PREPARED FOR

City of Sumner • Communications Department

SUBMITTED BY

Alpath Engineering

NEW, ACCESSIBLE CITY WEBSITE

A practical digital front door for the people who live, work, visit, and do business in Sumner.

PROJECT LEAD	TERM	PROPOSED TEAM
Matt Puleri	One year	2 named members

LETTER OF INTEREST

A website that works for residents and for the staff who maintain it.

Dear Carmen Palmer and
members of the City of Sumner
Evaluation Committee,

Thank you for considering Alpath Engineering for the design, development, and launch of a new, accessible City website.

Alpath is qualified to plan, design, build, move, test, and support content-rich websites. Our reference projects show that we can simplify complicated information, migrate code without losing content, improve performance, and remain accountable after launch.

Those qualifications would help Sumner create clearer paths to services, build accessibility into everyday publishing, prepare staff to maintain the website, and keep one accountable project lead involved from discovery through post-launch support.

We would welcome the opportunity to make Sumner's website easier for residents to use and easier for staff to maintain.

Sincerely,

Matt Puleri

Operator · Alpath Engineering

THE CASE FOR ALPATH

Qualified to build it. Focused on making it useful.

ARE WE QUALIFIED?

The goalposts move regularly where technology is concerned.

Matt has over 16k industry hours designing, building, migrating, and supporting websites that people rely on. His websites currently serve over 100k people each month. Anthony Damico adds experienced graphic-design support when the project calls for it.

HOW WILL THAT HELP SUMNER?

Residents get clearer paths. Staff get a safer system.

Sumner would receive an accessible, dependable website; editing tools that support good publishing; practical documentation and training; and a partner who remains responsible after launch.

Direct ownership

One lead connects resident needs, design, and delivery.

Repeat relationships

Every Alpath client is a repeat client.

Honest fit

Private-sector examples, applied to public accessibility and security requirements.

The proposed one-year process begins by listening to residents and staff, then moves through content organization, platform selection, design, development, migration, testing, training, launch, and post-launch support.



MATT PULERI

Operator • Project Lead

Matt would remain accountable for the website from discovery through launch and ongoing support.

PROPOSED RESPONSIBILITIES

- Lead conversations and decisions with City staff.
- Organize services, navigation, search, and page types.
- Recommend and configure the content management system.
- Guide design; build, connect, and test the website.
- Oversee migration, training, launch, and support.


RELEVANT QUALIFICATIONS

Direct experience building accessible websites, improving speed and reliability, moving sites between platforms, solving problems in existing systems, documenting work, and supporting clients after the initial project is complete.

FIRM OVERVIEW

A small team with a short path to an answer.

Alpath Engineering is a Pacific Northwest digital consultancy that brings website planning, visual design, development, accessibility, measurement, and ongoing support together. For Sumner, that means fewer handoffs and direct access to the people doing the work.

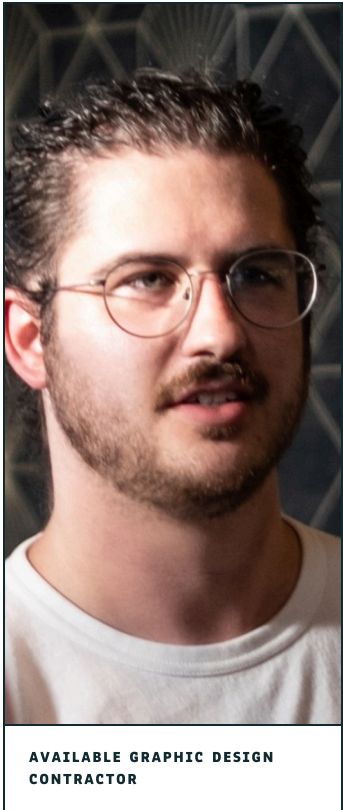

ANTHONY DAMICO

Senior Digital Designer • Contractor

Anthony is available for approved graphic-design needs such as visual assets, illustration, page graphics, and related design work.

EXPERIENCE

Senior Digital Designer at 500 Degrees Studio since 2019, following two years as a Junior Designer at Ibel Agency. His work includes web design and development, branding, advertising, campaign design, motion graphics, environmental and experiential design, packaging, and illustration.

RELEVANT SKILLS

Graphic design • Animation • Figma • Marketing

TOOLS

Illustrator • Photoshop • After Effects • Blender • Spline • Unreal Engine

[VIEW ANTHONY'S FULL RESUME](#)

ROLE CLARITY

Available support,
represented accurately.

- Anthony was recently brought into a separate project that remains in progress.
- He had no involvement in the three reference projects.
- Matt and Anthony will not be replaced without the City's prior approval.

THREE RECENT PROJECTS

Comparable website problems. Directly owned work.

These projects were undertaken within the past five years. They show that Alpath can move a large website safely, make information easier to find, improve performance, learn an unfamiliar system, communicate clearly, and continue supporting the client after launch.

01 2026 - Ongoing Lockhart Suver lockhartsuver.com Alpath moved a large WordPress website to a modern platform without changing the experience its users already knew. During the move, Matt improved the site's Google accessibility score from 74 to 96 and built a tool to recover the full image library when the old system could not export it cleanly. 74 → 96 GOOGLE ACCESSIBILITY SCORE Matt Puleri Matt handled all Alpath work for this project. He planned the move, built the new site and recovery tool, tested the work, managed launch, improved accessibility, and continues to support the website. Anthony Damico No involvement in this reference project. 206-659-8490	02 2023 - Ongoing Lennon Window Cleaning lennonwc.com Alpath rebuilt this Greater Seattle service website so customers could understand the services, find the right information on any device, and request an estimate with fewer steps. 300+ LEADS IN YEAR ONE Matt Puleri Matt handled all Alpath work for this project. He planned the site, organized the information, designed and built the pages, set up measurement, managed launch, and continues to improve the experience. Anthony Damico No involvement in this reference project. (425) 328-8827	03 2025 - Ongoing Distinctive Glass distinctiveglass.com When the previous developer was no longer available, Alpath learned the existing website, documented how it worked, completed the urgent updates, and gave the client a dependable path for future changes without forcing an unnecessary rebuild. Continuity DEPENDABLE WEBSITE SUPPORT Matt Puleri Matt handled all Alpath work for this project. He learned the existing system, diagnosed problems, completed updates, reviewed each release with the client, and provides ongoing support. Anthony Damico No involvement in this reference project. 206-659-8490
---	--	--

STANDARDS AND VERIFICATION

Accessible at launch and maintainable afterward.

Alpath would connect each requirement to page design, publishing guidance, testing, fixes, and launch approval.

APPLICABLE STANDARDS

01 WCAG 2.1 AA Use the City’s required accessibility standard to guide page design, content, forms, interactions, testing, and launch approval.	02 ADA Title II Treat equal access as a requirement throughout the project, rather than checking it only after the website is built.	03 Section 508 Connect the applicable requirements to page templates, staff guidance, testing, and a clear record of any fixes.	04 Washington OCIO Include Washington State accessibility policies in the project checklist and verify them before major approvals.
--	---	--	--

AUDIT AND REMEDIATION

01 Automated checks Run repeatable scans while the site is being built and before launch to catch code, structure, labeling, and color-contrast problems.	02 Keyboard & visual checks Make sure people can move through the site without a mouse, see where they are, zoom the page, use it on different screens, and recover from errors.	03 Screen-reader checks Test navigation, headings, forms, tables, messages, and common resident tasks with screen-reading software.	04 Content & document checks Review headings, links, image descriptions, reading order, page templates, and important downloadable documents.
--	---	--	--

A passing scan is not enough to approve launch.

Core tasks receive keyboard and screen-reader review; every issue has a priority, owner, evidence, and follow-up check.

CMS, MIGRATION, AND TRAINING

Make accessible publishing easier for City staff.

The platform would be selected after discovery, based on City needs rather than assumed in advance.

01 Choose the right platform Compare options based on accessibility, security, ease of editing, connections to City services, long-term support, ownership, and total cost.	02 Organize City information Create clear, reusable page types for departments, services, news, meetings, documents, alerts, contacts, facilities, and common questions.
03 Make publishing safer Give each staff member the right level of access, provide dependable page layouts, define review responsibilities, and make accessible choices easier.	04 Move content & prepare staff Decide what to keep, rewrite, or archive; move content in manageable groups; preserve old links; train staff; and provide clear instructions.



ONE-YEAR STARTING PLAN

Clear phases, decisions, and responsibilities.

The schedule would be confirmed with City staff after discovery, then managed through visible milestones and regular reviews.

01 Learn what is needed Weeks 1-4 · Meet with City staff, review the current website and its use, identify accessibility and technical problems, and agree on priorities and risks.	02 Organize services clearly Weeks 5-8 · Group information around the tasks residents need to complete, then plan navigation, search, page types, and connections to other City services.	03 Design & test the experience Weeks 9-14 · Create an accessible visual direction and working page examples, gather feedback, and agree on what must be true before the design is approved.
04 Build the website Weeks 15-26 · Configure the content management system, build page layouts and forms, connect outside services, set staff access, and improve speed and reliability.	05 Move content & verify the work Weeks 27-38 · Move content, preserve old links, involve staff in review, complete automated and hands-on accessibility checks, test security and capacity, and train editors.	06 Launch & support staff Weeks 39-52 · Launch in a controlled way, resolve issues quickly, provide documentation, review the live website, plan improvements, and discuss ongoing maintenance options.

Content migration and staff training begin before development is complete, so questions and accessibility improvements can be addressed while changes are easier and less expensive.

VISIBLE PROJECT CONTROLS

Protect the work, the schedule, and City information.

Quality and security are planned throughout the project instead of being postponed until launch.

QUALITY, SCHEDULE, AND COST

01 Keep the schedule visible Use clear milestones, owners, and weekly updates. Raise delays early when a decision, City input, or outside provider affects the schedule.	02 Control costs before work changes Prioritize the work, write down assumptions, explain the cost and schedule effect of a requested change before approval, and consider long-term operating costs.	03 Agree on quality before launch Define what “done” means, review accessibility and content, test common browsers and devices, document the work, and prepare launch and recovery checklists.
---	--	---

PUBLIC-SECTOR SECURITY

01 Reliable hosting Use a secure, monitored hosting setup with backups, recovery steps, speed targets, and availability appropriate for important City information and services.	02 Safe staff access Give staff only the access they need, protect administrator accounts, remove access when roles change, and use multifactor sign-in where supported.	03 Software updates Assign responsibility for updates, review third-party software regularly, test changes before release, respond to security concerns, and keep a current software list.	04 Forms & resident information Collect only what is needed, protect information while it is sent, define how long it is kept, limit spam and abuse, and review every outside service carefully.
---	---	---	---

A USEFUL PROJECT RECORD

City staff can see what changed, why, and what comes next.

Routine questions would generally receive a response within one business day. Outages, security concerns, and major service failures receive priority attention.

Communication and documentation • Weekly progress updates while work is active. • Reviews at each major stage before moving forward. • A shared list of issues, risks, decisions, and owners. • Accessibility findings and post-launch priorities. • Recorded training and written staff instructions. • Launch, recovery, and support procedures.	Commitments to the City • Matt Puleri remains project lead and Anthony Damico remains the named graphic-design contractor. • Neither named member nor any approved specialist will be replaced without prior City approval. • Additional specialists will be disclosed before assignment. • The City receives the agreed records, design files, guidance, instructions, and website materials in the final scope.
One-year professional-services period with the option to develop a maintenance plan	Controlled launch followed by review, issue resolution, and improvements

PROFESSIONAL REFERENCES

People who know our work.

01	Brad Kulkin Secure Back Office · Consultant	brad@securebackoffice.com 206-659-8490
02	Michael Neese Pro3 Accounting · Operator	michael@pro3accounting.com 319-594-8979
03	Supo Techagumthorn Washington Small Business Development Center · Certified Business Advisor	supo@wsu.edu 425-331-9775

Finally,

You are comparing several responses to the same challenge and likely have the great problem of picking between excellent options. As mentioned before, it is a badge of honor we wear at Alpath that **all of our clients all repeat-clients**. Gaining your trust would mean that we have the chance to earn your business again over the next year. We are confident we could do so.

Thank you
